



Prepared for

DTE Energy
One Energy Plaza
Detroit, Michigan 48226

2022 ANNUAL INSPECTION REPORT RANGE ROAD LANDFILL ASH DISPOSAL FACILITY

China Township, St. Clair County, Michigan

Prepared by

Geosyntec 
consultants

engineers | scientists | innovators

1420 Kensington Road, Suite 103
Oak Brook, Illinois 60523

CHE8242V-07

January 2023

TABLE OF CONTENTS

1.	INTRODUCTION.....	1-1
	1.1 Overview	1-1
	1.2 Purpose.....	1-2
	1.3 Report Organization.....	1-2
	1.4 Terms of Reference	1-3
2.	REVIEW OF AVAILABLE INFORMATION	2-1
3.	FACILITY DESCRIPTION.....	3-1
	3.1 Overall Site Description.....	3-1
	3.2 Design.....	3-3
	3.3 Construction	3-4
4.	VISUAL INSPECTION RESULTS.....	4-1
5.	INSTRUMENTATION MONITORING	5-1
	5.1 Surface Water and Groundwater Collection	5-1
	5.2 Groundwater Elevations and Offsite Capture System Monitoring	5-1
	5.3 RRLF CCR Monitoring Wells	5-1
6.	OPERATION ACTIVITIES	6-1
	6.1 Observations.....	6-2
7.	EVALUATION	7-1
	7.1 Design.....	7-1
	7.2 Construction	7-1

7.3 Maintenance	7-1
7.4 Operations	7-2
7.4.1 Operations Plan	7-2
7.4.2 Fugitive Dust Control	7-2
7.4.3 Run-on and Run-off Control	7-2
7.4.4 Inspections	7-3
7.4.5 Annual Visual Inspection	7-3
8. CONCLUSIONS and certification.....	8-1

LIST OF TABLES

Table 1: Available Information Reviewed for Annual Inspection

Table 2: Site Phasing Summary-December 2015 and Updated for 2019 Report

LIST OF FIGURES

Figure 1: Landfill Work Area Phasing Plan

Figure 2: Site Surface Water Flow System

LIST OF APPENDICES

Appendix A: Resume of the Qualified Professional Engineer

Appendix B: Range Road Landfill 2022 Annual Inspection Log and Photographs

1. INTRODUCTION

1.1 Overview

This 2022 Annual Inspection Report (AIR) was prepared by Geosyntec Consultants (Geosyntec) to provide the results of the annual inspection of the coal combustion residuals (CCR) Range Road Ash Disposal Facility (Landfill) located in China Township, St. Clair County, Michigan. The annual inspection was prepared to comply with United States Environmental Protection Agency (USEPA) Coal Combustion Residuals Rule (CCR Rule) published on April 17, 2015, (40 CFR 257.84) it's Amendments and applicable portions of Rule Parts A and B Implementations. Under the CCR Rule, the Landfill is an "existing landfill" per 40 CFR 257.53 and must be inspected by a qualified professional engineer on a periodic basis, not to exceed one year.

The Landfill is located approximately one mile west of the St. Clair River between Lake Huron and Lake St. Clair. The Landfill is licensed by the Michigan Department of Environment, Great Lakes, and Energy (EGLE), as a Coal Ash Landfill. The property encompasses 514 acres of which 446 are designated for landfill development. The EGLE Facility ID Number is 392562 and License Number 9603.

Filling operations at the site began in the 1950s. The Landfill has had an operating license since 1966. The current Operating License issued to DTE Electric Company (DTE) and defined as Number 9603 supersedes and replaces the previous license (#9395). During 2022, the Landfill accepted bottom ash, fly ash, and waste coal from the St. Clair and Belle River Power Plants. The Marysville Power Plant is included in the current license but has been decommissioned and no longer sends ash to the landfill.

The Landfill has multiple operating and planned phases defined by work areas as discussed in the Landfill Development Plan, design drawings, and draft drawings and memorandums on RRLF Waste Filling Sequence. Currently, nine work areas are certified closed and three areas are active. Areas D3, G2 and F3/D3 are active as identified in Figure 1. For construction purposes, Area G2 has been subdivided into three phases. Area G2 Phases I, II, and III (also referred to as G2 Phases 1, 2 and 3) have been approved for waste placement. Area G2 Phase 1 fill was completed, capped, and is now certified as closed. Area E was not included in a current waste filling sequence overall site plan (Draft September 26, 2017) and may not be needed depending on actual future volumes of CCR disposed of during the life of the plants. However, it is still identified in the current Operating License Number 9603, Dated May 15, 2020.

1.2 **Purpose**

The purpose of the inspection under the CCR Rule [40 CFR 257.84(b)(1)] is:

“...to ensure that the design, construction, operation, and maintenance of the CCR unit is consistent with recognized and generally accepted good engineering standards. The inspection must, at a minimum, include:

- (i) A review of available information regarding the status and condition of the CCR unit, including, but not limited to, files available in the operating record (e.g., the results of inspection by a qualified person, and results of previous annual inspections); and
- (ii) A visual inspection of the CCR unit to identify signs of distress or malfunction of the CCR unit.”

This is accomplished through periodic visual inspection (and photo-documentation) of the Landfill, review of construction certification documentation, review of available operating records, and review of instrumentation monitoring data and evaluations intended to detect signs of instability.

1.3 **Report Organization**

The remainder of this report is organized as follows:

- Section 2 – Review of available information: summarizes various historical documents that were reviewed as part of this inspection
- Section 3 - Facility Description: provides information about the facility
- Section 4 – Visual Inspection Results: summarizes visual observations during inspections of the Landfill
- Section 5 – Instrumentation Monitoring: discusses the instrumentation and monitoring program
- Section 6 – Operation Activities: describes the operations organization and activities
- Section 7 – Evaluation: evaluates the results of the annual inspection
- Section 8 – Conclusions: provides the overall conclusions of the annual inspection

1.4 **Terms of Reference**

The annual visual inspection was performed by Mr. Daniel G. Bodine, P.E. of Geosyntec whose qualifications as a “qualified professional engineer” under the CCR Rule are presented in Appendix A. DTE’s “qualified person” accompanied Mr. Bodine.

This report was prepared by Mr. Daniel G. Bodine, P.E. of Geosyntec. The senior review was completed by Mr. John Seymour, P.E., of Geosyntec. He is a qualified professional engineer per the requirements of §257.53 of the CCR Rule.

2. REVIEW OF AVAILABLE INFORMATION

Geosyntec reviewed the documents listed in Table 1 for the 2022 annual inspection. Geosyntec is not responsible for the accuracy of the documents reviewed that have been prepared by others and has prepared this inspection report based on good engineering judgement and data review. References to TRC refer to TRC Environmental Corporation, NTH to NTH Consultants, Ltd., AECOM to AECOM and Headwaters or Boral to EcoMaterial Technologies. As such, forms are being used with various names.

Table 1 Available Information Reviewed for the 2022 Annual Inspection

Title	Prepared by	Month and Year	Content with 2022 Update Status
2021 Annual Inspection Report - Range Road Landfill Ash Disposal Facility	Geosyntec Consultants	January 2022	Results of 2021 RRLF Inspection Report on Review of Documents and Files Related to the Operating Record and Conducting a Visual Site Inspection of the Facility.
Landfill Development Plan with Plan Sheets	TRC	Final November 2013	Overall Development Plan for Landfill Including Design, Construction, Surface Water Management, Operation, Monitoring and Site Closure. The 2013 Plan Remains Unchanged for the 2021 Inspection.
Range Road Solid Waste Disposal Area Operating License Renewal Application	DTE	April 2019	Operating License Renewal Application for the Range Road Ash Disposal Facility. See Below.
Range Road Ash Disposal Operating Number and License Facility No. 392562 License No. 9603	EGLE	May 2020	New Solid Waste Disposal Area Operating License, Including Terms and Conditions. License is Active and Supersedes and Replaces the Previous Operating License Number 9395.
Construction Certification /Soil Verification (Area G2) Range Road Landfill	MDEQ	September 2015	MDEQ Authorization for Waste Placement in Area G2 Northern Portion (Phase 1). Waste Placement in Area G2 Phase II was Active During 2022 Inspection.

Title	Prepared by	Month and Year	Content with 2022 Update Status
2019 Site Plan Figure 1 of DTE Range Road Operating License Number 9603.	TRC & Part of Operating License Application	Figure Date April 2019	Landfill Area Site Plan Showing Locations, Designations, Status and Phasing Legend. Used as Figure 1 in Geosyntec's 2021 and 2022 Annual Inspection Reports.
DTE Energy Company RRLF Area G2 Phase II Base Liner Draft Construction Plans	NTH	March 2018	Area G2 Phase 2 Base Liner Construction Plans-No Change Reported for 2022.
Construction Certification/Soil Verification (Area G2 Phase III)	EGLE	April 7, 2022	Approval of Supplemental Certification of Base Liner Grades for Area G2 Phase III, i.e., Approval for Waste Placement.
DTE Range Road Waste Filling Sequence with RRLF Estimated Life Expectancy and Capacity Summary	NTH	April 2018	Ash Volumes & Estimated Fill Volumes for Closure for Areas G2 Phases I, II & III, and Area F3/D3. Estimated Dates for Closure Start Given. No Change Reported for 2022.
Certification of Base Liner Grades (Area G2-13.1 Acres) DEQ Review Letter	State of Michigan DEQ	September 2018	DEQ's Review Indicating Certification is Consistent with the Requirements of Part 115. This is G2 Phase II Area Reported as 13 Ac in Current Operating Permit.
Soil Erosion and Sedimentation Control Permit No. SE2017-41	St. Clair County Health Department	April 2017	Permit Issued April 10, 2017 and Expired on April 10, 2019. Work was completed and Permit was Closed Out without Issue.
NPDES Permit No. MIR11436	State of Michigan DEQ	June 2017	Permit Authorizing Discharge of Storm Water from Construction Activities at DECO-Belle River Pit (Site Name). Permit has been Closed Out 4-10-19.
NPDES Permit No. MI0038172	State of Michigan DEQ	October 2018	Permit for discharge from the Belle River Power Plant and Blue Waters Energy Center

Title	Prepared by	Month and Year	Content with 2022 Update Status
Surface Water Flow Figure 2 (Working Copy)	TRC	December 2015	Plan of Ditch and Surface Flow Directions, Staff Gauge & Piezometer Locations. Copy used as Reference for Ditch & Surface Flow Locations in this report.
Closure Plan for Existing CCR Unit 40CFR 257.102 (b)	AECOM	October 2016	Closure Plan Description, Inventory and Area Estimates, Schedule and PE Certification. Plan Remains Unchanged.
Post Closure Plan for Existing CCR Unit 40CFR 257.104	AECOM	October 2016	Post Closure Plan Description, Monitoring & Maintenance, Owner Operator Requirements and PE Certification. Plan Remains Unchanged.
Run-On/Run-Off Control System Plan for CCR Disposal Facility-Range Road	AECOM	October 2016	Plan to Address §257.81(c) of the USEPA CCR Final Rule. Appendices Included Historical Design Drawings and HydroCAD Analysis Output. Plan Remains Unchanged.
Groundwater Contour Maps October 2021 and February 2022 Provided in TRC 4 th Quarter 2021 and 1 st Quarter 2022 Reports	TRC	October 2021 & February 2022	Groundwater Flow Directions and Elevations Outside & Inside of Slurry Wall. Perimeter Ditch Water Elevations at Staff Gauge Locations.
Area F3 Cap Material Borrow Areas	NTH	August 2016	Identifies Approx. Quantities of F3 Cap Topsoil, Clay and Inert Fill Required and Quantities of G3 Area Borrow Available.
Range Road Area F3 Final Closure – Existing Site Plan Draft - Dwg No. 6C664-158	DTE	February 2017	Drawing Showing Landfill Areas Including Future Portions of Area G that can be Used for Active Topsoil and Clay Borrow.
DTE Energy Company - Range Road Area F3 Final Closure - Drawings	NTH	March 2017	Bid Issue Cover Drawing Listing Sheet Index of 8 Drawings.
Range Road Landfill Coal Combustion Residuals Fugitive Dust Plan-Rev 1	DTE	July 2019	Plan Certified by Professional Engineer to 40 CFR 257.80(b)(7) Revision 1. Plan was Updated in 2019.

Title	Prepared by	Month and Year	Content with 2022 Update Status
DTE Electric Company – Range Road Landfill Coal Combustion Residuals Annual Fugitive Dust Reports	DTE	November 2020 & November 2021	Annual Fugitive Dust Control Report Pursuant to 40CFR 257.80(c). Descriptions and Actions Taken to Control CCR Fugitive Dust.
Updated Fugitive Dust Plan	DTE	Rev 2 of Plan Dated 11/9/2021	Rev 2 of Plan was Submitted to EGLE. Rev 8 of Fugitive Dust Control Program Dated 3/22/22 was also Submitted per DTE.
CCR Groundwater Monitoring Well Locations (Working Copy)	TRC	April 2016	Plan Showing Name & Locations of Seven (7) Monitoring Wells Around Landfill.
Groundwater Potentiometric Elevation Summary Figure 7	TRC	October 2017	Groundwater Elevation Summary for the 7 Groundwater Monitoring Wells Numbers 16-01 thru 16-07.
4 th Quarter 2021 & 1 st Quarter 2022 Groundwater Elevation Monitoring Tables 1 and 2	TRC	October 2021 and February 2022	Summary Tables of Groundwater Well/Piezometer and Perimeter Ditch Staff Gauge Elevation Monitoring.
MDEQ WMRPD Q3 FY18 Inspection Report	Michigan DEQ	July 2018	2018 3 rd Quarter Inspection Report
MDEQ WMRPD Q4 FY18 Inspection Report	Michigan DEQ	September 2018	2018 4 th Quarter Inspection Report Recommend Removal of Top Cover Woody Vegetation. Per 2020 & 2021 inspection woody vegetation has been removed.
MDEQ/EGLE MMD Q3 FY20 & Q1 & Q3 FY21 Inspection Reports	Michigan EGLE	June 2020; January & May 2021	Facility in Compliance Reported.

Title	Prepared by	Month and Year	Content with 2022 Update Status
EGLE MMD FY21 Q1, Q2, Q3 & Q4 Inspection Letters	EGLE	January, April, May & November 2021	Facility reported to be In Compliance
EGLE MMD FYQ1 Inspection Letter	EGLE	January 2022	Facility reported to be In Compliance
DTE 2018 1 st , 2 nd , 3 rd and 4 th Quarterly Comprehensive Inspection Log (s)	DTE	March, May, August and November, Respectively 2018	Inspection Condition and Notes: Final Cover for Areas, Surface Water Ditches & Signage.
DTE 2020 3 rd & 4 th and 2021 1 st , 2 nd , 3 rd & 4 th Quarterly Comprehensive Inspection Log (s)	DTE	July & October 2020; January, April, July & October 2021	Inspection Condition and Notes: Final Cover Capping for Area G2, Surface Water Ditches & Signage and Discussions on Final Cover Mowing.
DTE 2022 1 st Quarter Comprehensive Inspection Log	DTE	March 2022	Inspection Condition Summary and Notes Provided in Log in Appendix B.
2020 & 2021 Selected Weekly General Inspection Log (s)	DTE	Weekly Logs March 29, 2020 thru June 1, 2020 and February 21, 2021 thru May 2, 2021	Inspection for General Site, Waste & Nuisance Control, AST Spill Cleanup, Final Cover, Leachate & Surface Water Control & Pump Operation. Viewed Requested Weekly Logs.
Weekly General Inspection Logs	DTE	May 10, 2021 thru April 3, 2022	Key Observations NW Panel/Pump Repair May-June, Tree Removal on Fencing. October G2 Phase I Seeding & Cover Erosion Noted in Winter. Reseed Planned in Spring '22. Minor Soil Hole/Removal Beneath Fence but All Fencing Intact.

Title	Prepared by	Month and Year	Content with 2022 Update Status
Environmental Outside Rounds Log Sheet (A Daily Inspection Log)	DTE	Not Viewed	Daily Plant Environmental Inspection Log Sheet. Record Unusual Conditions, Gate Conditions, Flow Meter Readings, etc.
Groundwater Monitoring System - Summary Report	TRC	October 2017	Summary Report Figure 2 Used for Identifying Monitoring Well Locations.
Mobil & Fixed System Equipment Training Record	Headwaters, Inc. or Boral. Now EcoMaterial Technologies	August 2017	Classroom, Field Discussion, Observation, Operation and Unassisted Operation Training Record for New Employee. No Updates Provided for 2019, 2020 or first Part of 2021. DTE Indicated No Changes in 2021 and Spring 2022, Other Than Company Name Change.
Landfill Contractor Construction Training Records	Headwaters, Inc. or Boral. Now EcoMaterial Technologies	None Provided	No New Training Records Provided for the 2021 Inspection.
Appendix D to §1910.134 (Mandatory) Information for Employees Using Respirators When Not Required Under the Standard	Headwaters, Inc. or Boral. Now EcoMaterial Technologies	Sept. 9, 2017	Discussion of Respirator Use, Selection, Cleaning, Related Hazards and Respirator Labeling was Provided for the 2017 Inspection. No Updates for 2020 – 2022, Other Than Company Name Change.
Employee Acknowledgement of Receipt of Safety Consequence Policy	Headwaters, Inc. or Boral. Now EcoMaterial Technologies	Sept. 9, 2017	Employee Acknowledgement of Reading, Understanding of Policy and Safety Guidelines. Copy Applicable to New Employees for 2017. No Updates for 2020 – 2022, Other Than Company Name Change.
Copy of Construction Drawings for G2 Phase 2 Base Liner	NTH	April 23, 2018	Area G2 Phase 2 Base Line Construction Drawings. Drawings for G2 Phase III not provided or requested.
Partial Closure Certification (Area F3)	MDEQ	May 22, 2018	Approval Letter for Partial Closure. No Updates for 2020 - 2022.

Title	Prepared by	Month and Year	Content with 2022 Update Status
Constructions Documentation Report – Area G2 Phase I Closure	NTH	January 2022	Construction Documented and Certified by Engineer.
Area G2 Phase I Closure Certification Approval	EGLE	January 2022	Closure Certification Reviewed by MMD and Approved by EGLE

3. FACILITY DESCRIPTION

3.1 Overall Site Description

The overall site facility property is composed of the 514 acres of which 446 are designated for landfill development. The Landfill work areas are currently divided into fourteen work areas, nine that have been identified as “Certified Closed”, three identified as “Active” and two identified as “Unconstructed”. The work areas are listed below in **Table 2** and shown in **Figure 1**. **Figure 1** is taken from the 2020 Site Plan provided in the Solid Waste Disposal Area Operating License effective April 22, 2019.

Table 2 Site Phasing Summary – 2019-2020

<u>Area</u>	<u>Status</u>	<u>Size (Acres)</u>	<u>Comments</u>
A	Closed	7	Certified Closed, May 17, 2002
B	Closed	102	Certified Closed prior to September 2, 1999
B1	Closed	9	Certified Closed prior to September 2, 1999
C	Closed	16	Cert. Report Approved August 25, 2009
D1	Closed	21	Cert. Report Approved August 25, 2009
D2	Closed	10	Cert. Report Approved August 25, 2009
D3	Active	3	Interim Cover Placed at Time of Inspection
E	Unconstructed	117	No Cell Construction or Waste Placed
F1	Closed	17	Cert. Report Approved January 4, 2010
F2	Closed	12	Cert. Report Approved February 28, 2013
F3	Closed	17	Closed Reported Certification Approval
F3/D3	Active	5	Active Per Operating License, April 2019
G1/G3	Unconstructed	56	No Cell Construction or Waste Placed 2019
G2	Active	<u>54</u> **(Total Permitted)	
	G2 Phase 1		(Waste Capped and Closure Certified Complete)
	G2 Phase 2		(Waste Placement In Progress)
	G2 Phase 3		(Liner Construction Completed and Approved for Waste Placement)

** Acreage from DTE Renewal Permit Application

The Landfill includes perimeter ditches, roadways, a perimeter slurry wall, earth berms, a 10 Acre NPDES Stormwater Detention Basin (SDB) and basin pump house. The basin has also been referred to as the sedimentation basin in some of the reviewed documents and figures. The SDB is located in the southeast corner of the property; the slurry wall, reported to be approximately 10

to 15 ft deep, surrounds the entire landfill along the property perimeter. The perimeter ditch surrounds the entire Landfill connecting and draining to the SDB (Figure 2). The pump control areas for these systems and the SDB pumping system were observed during the 2021 annual inspection.

The Landfill is a dry-handled (conditioned) CCR landfill licensed by EGLE as a Coal Ash Landfill with maximum 4 horizontal (H) to 1 vertical (V) final cover side slopes and 3 H to 1 V or flatter interim cover slopes. The current revised estimated annual total CCR disposal rate is 160,000 in-place cubic yards/year (average) based on historical CCR production rates and calculations of volumes by NTH using aerial flyovers performed in 2019 and 2021. The currently permitted areas of the Landfill are expected to handle the anticipated volume of CCR through the life of the landfill.

The Landfill has a native, in place clay liner ranging from 86 to 188 feet thick and is present beneath the entire Landfill. A thin discontinuous near-surface sand seam is present beneath the northeastern portion of the landfill; however, a slurry wall and perimeter ditch system were designed and installed to preclude any off-site flow from the sand seam.

3.2 **Design**

The Landfill design and operation is summarized in the Landfill Development Plan, Remedial Action Plan, Run-on/Run-off Control System Plan and the Quarterly Monitoring Reports. The key components of the Landfill include:

- Perimeter slurry wall keyed into top of 70-foot thick subbase clay layer;
- Perimeter drainage ditch capturing surface water and near surface groundwater;
- 10-Acre SDB collecting ditch water and pumping to plant;
- Two off site groundwater capture systems collecting water in the shallow sand seam;
- Final Cover installation from top to bottom that includes:
 - 6-inch thick vegetated topsoil layer (erosion layer);
 - 24-inch thick infiltration layer (select clay layer with hydraulic conductivity, $k \leq 1 \times 10^{-7}$ cm/sec);
 - Maximum 4H to 1V FINAL side slopes;
 - Minimum 1% grade top of closed areas and minimum 2% grade for areas to be closed in the future, and

- Phasing plans and special conditions detailed in drawings, plans and license.
- Closure and Post Closure Plans

Landfill design and construction are supported by construction phasing plans, surface water management plans and details, site operation (waste placement) plans and details, and leachate and environmental monitoring plans and reporting. Additionally, landfill monitoring systems maintenance and inspection, and site closure and post closure plans with long term care procedures are covered.

3.3 **Construction**

The Landfill has been operating since the 1950s. The Landfill Operating License discusses the work areas (see Section 3.1), references design, construction and monitoring documents submitted by DTE and includes conditions and criteria required for the Landfill operation, phase construction and monitoring. A renewal permit, License Number 9603 effective May 15, 2020, was issued to DTE by the EGLE. Closure and Post Closure Plans in accordance with 40 CFR 257.102 (b) and 40 CFR 257.104, respectively, have been prepared with an operating record date of October 17, 2016. A permit for NPDES discharge of storm water has been issued by EGLE.

The Landfill Development Plan discusses site operations in Section 4 of the plan. Included are discussions on dust control, noise control, odor control, and access and security requirements, among other operating aspects. CCR filling procedures and requirements for construction observation and documentation are also included in the development plan.

4. VISUAL INSPECTION RESULTS

The annual inspection on site was completed on April 19, 2022. The annual 2022 inspection log and photographs are presented in **Appendix B**.

In summary, no evidence of landfill instability, significant perimeter slope erosion, or detrimental settlement was noted. The perimeter ditch, perimeter slurry wall, and pumping of water in the SDB appeared to be working as designed and in accordance with recognized and generally accepted good engineering standards.

The northwest groundwater capture system and collection has had its two pumps replaced in late 2017. The pumps are used to transfer the captured water to the perimeter ditch for gravity flow to the SDB. At the time of the inspection DTE tested each pump for operation. The pump control switches have been placed in the auto position and pump operation confirmed by DTE.

Specific results of the visual inspection are summarized below and in the **Appendix B Inspection Log**. Photographs are provided in **Appendix B**. The weather on the day of the inspection was cloudy with temperatures ranging from 32° F to a high of 43° F by mid-day. Light snow had occurred at the end of the previous day and evening, but no precipitation occurred during the inspection.

SDB: The SDB appeared in good condition. Basin slopes and intake screens are shown in Photographs 1, 2 and 4. The pump control panel is shown in Photograph 3. Pumps 1 and 2 were not running at the time of the inspection, but there was no indication of pumps taken out of service. The basin intake screen was unblocked as shown in Photograph 2.

Landfill Final Cover: Closed work area phase covers were intermittently inspected by this Engineer including slopes. Conditions appeared good considering agreements approved with EGLE allowing trees remaining along and on the downstream slope at the north end of the Landfill, predominately in historical Areas A and B. These slopes were observed from the perimeter toe. The top cover was covered with some very light snow but appeared well vegetated. The entire cover was mowed during 2021 as part of on-going maintenance work. No woody vegetation was observed. Photographs 33, 34, and 36 show typical cover surface conditions in Areas F1, F2, and part of B.

The closed and active areas locations are identified on **Figure 1** and listed in **Table 2**.

There were no observed areas of pooled water on closed areas of the top cover however travel was limited to walking and not vehicle travel.

Some of the final cover swales, downslope drains (down-chutes) and downslope ditches were observed as part of the final cover inspection. All observed appeared in acceptable condition (see also next paragraph). However, the large downslope riprapped drainage channel located at the west intersection of Areas F1 and F2 and shown in Photograph 29 continues to show some bottom/bedding area erosion exposing gully like soil rutting under the riprap based on previous inspection. The voids between and under some of the riprap stones could possibly be filled with smaller bedding type stone as a repair. The original design was unclear as to the type of bedding that was provided. The DTE inspector indicated that no repair or maintenance work has been done and their observations indicate that the condition is stable and no repair or expedited maintenance work is required at this time.

Surface erosion repair and re-seeding along the east side of the main haul road to the top of the closed landfill area was completed in 2022 after the annual inspection. DTE provided Photos 53 and 54 showing the completed repair.

In conclusion, the top and final slopes of the closed landfill final cover areas appeared well vegetated and are consistent with recognized and generally accepted good engineering standards.

Active Area G2: Area G2 Waste Filling Sequence has been divided into Phase 1, Phase 2 and Phase 3 for purposes of liner construction and certification. The G2 Phase 1 area ties in with Area F2. Area G2 Phase 1 final clay cover and initial seeding was completed at the time of the annual inspection. Photographs 30, 31, 32, 37, 38 and 39 show the clay cover on the top and slopes, again at the time of the inspection. Some medium size erosion gullies were observed on the east side slope and top swale as shown in Photos 38 and 39. Since the April inspection DTE has repaired the erosion and reseeded the area top and slopes where needed. Photos 40, 41 and 42, taken provided by DTE, show repaired and well vegetated slope areas that are also typical of the top cover. Area G2 Phase 1 Closure was certified and now approved by EGLE.

New or freshly conditioned CCR waste was observed in Area G2 Phase 2. At the time of the inspection there was hauling, and placement activities as shown in Photographs 44 and 45. Placement and compaction procedures of conditioned CCR would closely follow the Ash Filling Procedures discussed in the Landfill Development Plan. However, during the inspection only placement and grading was occurring.

Perimeter Ditch System: The Perimeter Ditch System is shown on **Figure 2**. Flow through the ditch system is maintained and monitored by DTE to ensure adequate flow to the SDB. Vegetation in the ditches is well established and is routinely maintained. Review of the DTE 2021 and 2022 weekly and quarterly inspection reports indicated that ditch vegetation maintenance was completed for several portions of the perimeter ditch alignment along the northeast, north, west and southwest sides of the Landfill and along the SDB perimeter slopes. Observations and discussions with DTE

during the 2022 inspection indicated that the ditch cleaning and maintenance program is continuing. Requested 2022 weekly and quarterly inspection reports were reviewed. The SDB and perimeter ditch slopes that were cleared of excessive vegetation appeared stable as shown in Photographs 5, 6, 9, 11, 12, 15, 17, 20, 21, 25, 26 and 27. Ditch maintenance schedule modifications are subject to the needs of the site.

A ditch staff gauge system is used to monitor water level in the perimeter ditch. Review of the monitoring summary tables prepared by TRC for the 4th Quarter of 2021 and 1st Quarter of 2022 were reviewed and confirmed that ditch flow directions were acceptable. Three staff gauge water level elevations (SG-8, SG-10 and SG-11) in the 1st Quarter 2022 measurements indicated that the water at their locations was frozen and may be stagnant and not flowing in either ditch direction. Review of the elevation data for the remaining gauges all indicated acceptable flow directions, as did the 4th Quarter 2021 review. Photographs 5, 6, 9, 11, 12, 15, 17, 20, 21, 25, 26 and 27 show typical ditch conditions at various staff gauge and culvert locations.

The slurry wall is located outside of the perimeter ditch and along the property boundary. Many location markers remain identifying the below ground slurry wall location.

Operation Activities Including Waste Placement: The landfill operating contractor is Eco Material Technologies (formerly named Boral and previously Headwaters). The landfill field office was closed when checked, or no one present at the time a visit was made. However, field placement activities were ongoing and the DTE Inspector indicated that he knew of no new personal added to the work force.

DTE provides operation monitoring through daily log monitoring of pumping from the SDB (NPDES pond flow monitoring) and weekly and quarterly monitoring of check list items. SDB Pump operation and flow is inspected by DTE daily and weekly.

Record Keeping: At the start of the 2022 annual inspection, records of current DTE monitoring inspections and new or updated reports were discussed with the landfill engineer. Copies of records requested were electronically transmitted and reviewed for this report.

The current operating license dated May 15, 2020 lists many documents that have been submitted to the EGLE by DTE as part of the landfill design, plan preparation, construction certification and documentation, surface and groundwater monitoring, and landfill operation. The records for the Landfill appear comprehensive.

5. INSTRUMENTATION MONITORING

5.1 Surface Water and Groundwater Collection

Surface water and groundwater monitoring are conducted under a monitoring plan approved by EGLE. The surface water that falls within the landfill waste areas and within the perimeter ditch system is collected by the ditch system and flows, for the most part by gravity, to the SDB, as shown in **Figure 2**. An exception to this is the perimeter ditch located at the northwest corner of the property where the ditch water is collected and pumped to a portion of the ditch on the north side which gravity drains to the SDB. The perimeter slurry wall installed along the property line and outside of the ditch and basin system supplements and supports surface water collection as well as contains and directs any near-surface groundwater to the perimeter ditch.

Monitoring of the ditch water collection is accomplished through ditch visual inspection and ditch slope and bottom maintenance, review of water elevations from a series of thirteen (13) staff gauges and implementation of EGLE approved monitoring plans. Reporting of the monitoring is summarized in tables prepared by TRC. Review of the ditch water levels for the staff gauges show that the water gradient flows to the SDB. The review is provided in report Section 7.3 on ditch maintenance.

The perimeter ditch also collects near-surface groundwater that occurs along the east side of the property where near-surface sand is located above the subsurface thick layer of clay. The slurry wall in that area, with the top elevation higher than the groundwater elevation, acts as a groundwater flow barrier and supports collection by the perimeter ditch.

5.2 Groundwater Elevations and Offsite Capture System Monitoring

Monitoring well and piezometer locations are shown on **Figure 2** and monitoring water depths and elevations summarized in tables prepared by TRC. Groundwater elevations and flow directions typically indicate that the site-wide slurry wall and perimeter ditch network continue to perform as designed to prevent shallow groundwater beneath the RRLF site from migrating off-site. The DTE landfill engineer also monitors the ditch water flow and includes a map or figure showing ditch flow directions as part of their quarterly inspection reports.

5.3 **RRLF CCR Monitoring Wells**

During the 2022 annual inspection locations of seven (7) groundwater monitoring wells were observed. Observations indicated that that the monitoring wells were well protected with casing caps or covers keyed and locked. Photos 7 and 13 show typical examples of well protections.

6. OPERATION ACTIVITIES

Operations are defined in Section 4 of the Landfill Development Plan. The following operation control measures are described in the plan:

1. Hours of Operation
2. Waste Types
3. Traffic Routing
4. Lines and Grades
5. Nuisance Control (includes Fugitive Dust Control)
6. Police and Fire Protection
7. Access Control
8. Inclement Weather Operations
9. Drainage and Erosion Control
10. Record Keeping
11. Personnel and Equipment
12. Ash Filling Procedures
13. Leachate Management
14. Environmental Monitoring

Engineering design and construction related to the Landfill design, waste type and volumes, subbase grades, site phasing, final cover, surface water management, construction observation and documentation, and final closure and long-term care are included in the Landfill Development Plan. The plan was written by DTE/TRC in November 2013 and contained the Landfill operating license valid at that time.

In addition, the following plans and inspections are currently required by the CCR Rule:

- Weekly inspections by a qualified person,

- Dust control in accordance with a Fugitive Dust Control Plan,
- Preparation and Implementation of a Run-on/Run-off Control System Plan,
- Preparation of the Closure Plan for the Existing CCR Unit, and
- Preparation of the Post-Closure Plan for the Existing CCR Unit.

These plans were available for inspection during this or previous visits and are included in the project document file. The Annual Fugitive Dust Control Reports dated November 18, 2022, was reviewed. There was one citizen complaint on May 9, 2022 which was investigated by DTE and found to be an isolated case due to very high winds. The incident was discussed with the contractor and measures implemented to prevent reoccurrence. No other complaints were received. DTE weekly inspection reports for the winter of 2021 and 2022 were also reviewed for this report.

6.1 **Observations**

It was identified that overall the Operations Plan was being followed. Documentation was reviewed that demonstrated that the Operations Plan was being followed in a method "...to ensure that the design, construction, operation, and maintenance of the CCR unit is consistent with recognized and generally accepted good engineering standards" in accordance with the CCR Rule.

Operating control measure items appeared to be compliant with the Landfill Development Plan. There is a full-time DTE guard shack or building near the entrance of the Landfill and the Landfill is surrounded by security fencing and locked gates.

7. EVALUATION

7.1 Design

The Landfill design was completed by TRC and is well documented in the references listed in the current Landfill Solid Waste Disposal Area Operating License, dated May 15, 2020, and the Landfill Development Plan, dated November 2013.

7.2 Construction

Construction of final cover phase work areas is being well documented in area closure documentation reports by NTH. Construction certification or documentation reports or portions of those reports were viewed during the 2015 and 2016 annual inspection for work areas C, D1, D2, F1 and F2 and they were signed by a professional engineer licensed in Michigan. A partial closure certification letter for Area F3, dated May 22, 2018, was prepared by MDEQ. Clay for the capping was excavated as part of subgrade excavation within portions of Area G2. CCR hauling and placement in Area G2 Phase 2 was occurring on the date of the 2022 inspection. DTE indicated that Area G2 Phase 1 was capped, seeded and construction documentation report prepared. Shortly after the annual inspection the construction certification was approved by EGLE.

7.3 Maintenance

Maintenance of final cover vegetation and erosion control has been identified by the DTE qualified person as an ongoing activity based on results of weekly inspections. Quarterly Comprehensive Inspection Logs lists specific comments on the status, schedule and results of maintenance activities. These listed activities reviewed included pump operation and maintenance, closure cover construction, ditch repairs and vegetation clearing, and slope and cover vegetation maintenance. Many of the activities mentioned are necessary to maintain operation and consistent flow direction of water collected by the perimeter ditch. Review of the DTE 2021 and 2022 weekly inspection reports did indicate that some onsite pump and panel maintenance activities were necessary for the NW Capture System. The 2022 inspection indicated that those considered significant and necessary were performed.

Tables summarizing staff gauge water elevations recorded during the 4th Quarter 2021 and 1st Quarter 2022 indicated that the ditch flow direction is again in agreement with the stated design and flow to the SDB.

Control of vegetation growth in the site ditches has been identified by DTE as a routine maintenance activity. Observations indicated that the perimeter ditch alignment is being cleared of excessive vegetation on a routine but as-needed schedule basis.

Results of this inspection indicates that the ditch maintenance program is progressing according to plans or ahead of schedule. Photographs of ditch maintenance results are provided in Appendix B and were discussed in Section 4.

7.4 **Operations**

7.4.1 Operations Plan

The Landfill Development Plan serves as DTE's main operations plan for the landfill. The plan has been discussed in previous AIRs and has again been reviewed as part of this AIR. The plan has not been revised. The landfill ash fill contractor in 2018 made improvements in following the plan's CCR placement and compaction procedures and appears to be continuing in Content with 2022 Update Status 2022 with the improved procedures.

Records by DTE, such as Landfill weekly inspection logs were provided as part of the annual inspection information. The inspection log forms were recently updated and are consistent with recognized and generally accepted good engineering standards.

7.4.2 Fugitive Dust Control

A Fugitive Dust Control Plan Rev 1, dated July 2019, was provided by DTE. Fugitive Dust Control is also discussed in the Landfill Development Plan. Annual Fugitive Dust Reports dated November 18, 2022 was provided for review. The report summarized CCR fugitive dust control actions, listed citizen complaints, if any, and provided discussion of any corrective actions taken for the period November 1, 2021 through October 31, 2022. There was one citizen complaint which was addressed by DTE, as mentioned above.

During the site inspection there were no observed dust clouds or active dust control activities. There were CCR hauling trucks or construction equipment operating. Light snowfall had occurred the night before the inspection and the roads that the inspection team traveled were dust free. Basin water is typically used for dust control when needed and signs limiting the use of the water in areas near the construction entrances have been posted by DTE.

Dust control operations at the site are considered consistent with recognized and generally accepted good engineering standards.

7.4.3 Run-on and Run-off Control

Run-on and run-off control are maintained by final cover temporary or permanent berms, the perimeter ditch system, the offsite pumping systems and the SDB pump and discharge system. The Run-on and Run-off Control System Plan was updated in 2021, and appears to be consistent

with recognized and generally accepted good engineering standards in accordance with the requirements of 40 CFR 257.81(c).

7.4.4 Inspections

Weekly and quarterly inspections have been ongoing and documented by qualified persons. Inspections reviewed have been discussed and are consistent with recognized and generally accepted good engineering standards, based on available information.

7.4.5 Annual Visual Inspection

This annual visual inspection did not identify any evidence of structural weakness or instability. The inspection did confirm that there had been slope erosion gullies on the east slope of Area G2 Phase 1. However, DTE confirmed and provided photographs of vegetation growth that these areas were repaired and reseeded as planned during the spring 2022. The perimeter ditch, perimeter slurry wall, offsite capture system pumping, and collection appeared to be working as designed and in accordance with recognized and generally accepted good engineering standards.

8. CONCLUSIONS AND CERTIFICATION

The annual visual inspection did not identify any evidence of structural weakness or instability.


Based on the annual inspection results and review of the available data, the Landfill was designed, constructed, operated and maintained in accordance with generally accepted good engineering standards.

Certified by:

Daniel G. Bodine

Date January 09, 2023

Daniel G. Bodine, P.E. - Michigan P.E. No. 6201051139
Senior Consultant



Plot Data

Design File: J:\DTE\St Clair Co\320507\0000\320507.0000.01.plt
 TFEor#Plot Date = Thu Apr 11 08:24:00 2019
 Plot File = J:\DTE\St Clair Co\320507\0000\320507.0000.01.pdf
 Pen Table = \\msn-plot\neQuorum8\BL\MSV8 - KIP PDF - HALF WT.tbl
 Levels On = 1-63


Reference Files

Ref. File 1 = J:\DTE\St Clair Co\320507\0000\REF\hmc - 2013-04-27.cpn
 Ref. File 2 = J:\DTE\St Clair Co\320507\0000\REF\hmmrmt.dgn
 Ref. File 3 = J:\DTE\St Clair Co\320507\0000\REF\proposed.dgn
 Ref. File 4 = J:\DTE\St Clair Co\320507\0000\REF\8x11bdr.dgn

Logical Names

Levels

:1) 45-50,53-56,58,59,61,63
 :2) 7-10,18,29,30
 :3)
 :4) 1-63

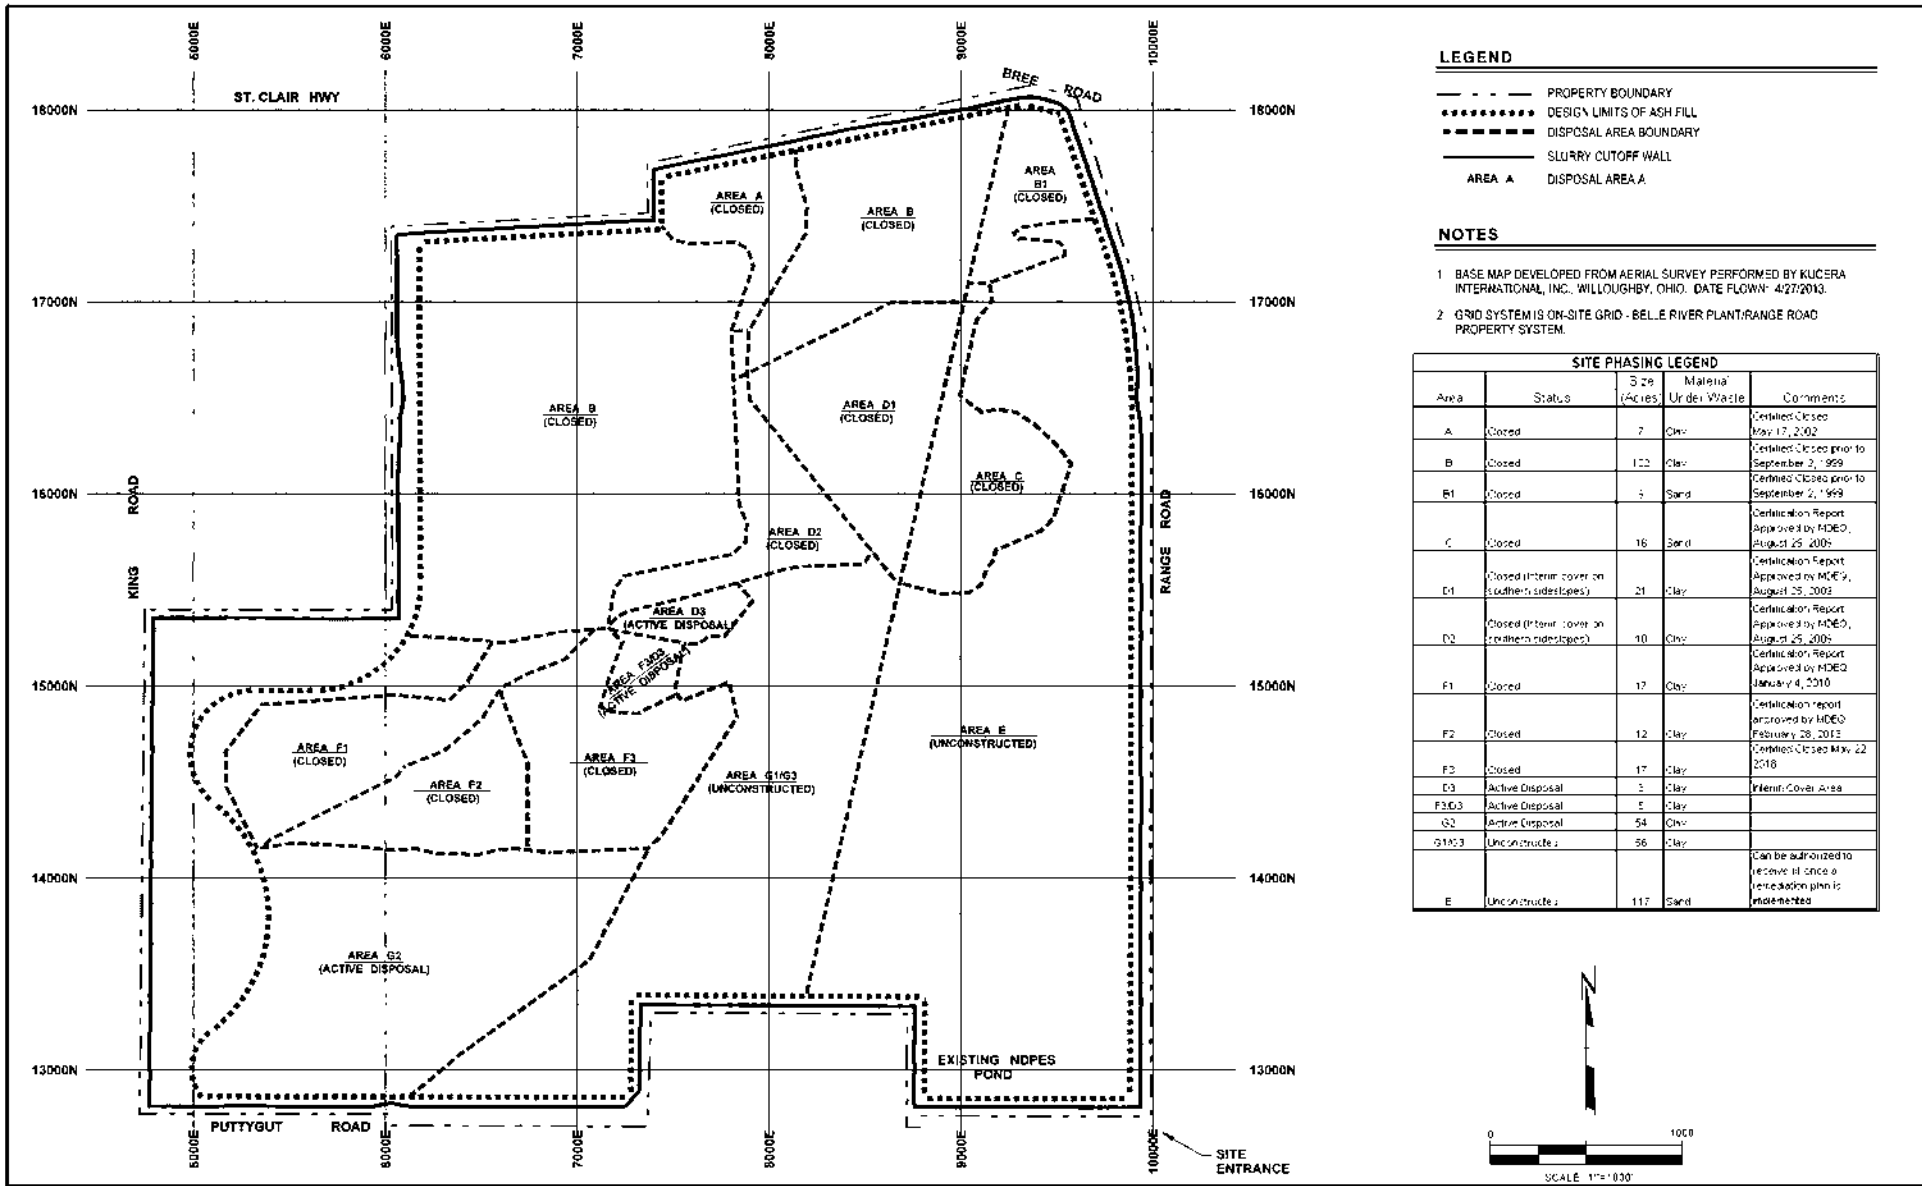


LEGEND

- PROPERTY BOUNDARY
- DESIGN LIMITS OF ASH FILL
- DISPOSAL AREA BOUNDARY
- SLURRY CUTOFF WALL
- AREA A DISPOSAL AREA A

NOTES

- 1 BASE MAP DEVELOPED FROM AERIAL SURVEY PERFORMED BY KUCERA INTERNATIONAL, INC., WILLOUGHBY, OHIO. DATE FLOWN: 4/27/2013.
- 2 GRID SYSTEM IS ON-SITE GRID - BELLE RIVER PLANT-RANGE ROAD PROPERTY SYSTEM.

SITE PHASING LEGEND				
Area	Status	Size (Acres)	Material/Under Waste	Comments
A	Closed	7	Clay	Certified Closed May 17, 2002
B	Closed	122	Clay	Certified Closed prior to September 2, 1999
B1	Closed	5	Sand	Certified Closed prior to September 2, 1999
C	Closed	16	Sand	Certification Report Approved by HDEQ, August 15, 2005
D1	Closed (Interim cover on Southern sideslopes)	21	Clay	Certification Report Approved by HDEQ, August 25, 2005
D2	Closed (Interim cover on Southern sideslopes)	10	Clay	Certification Report Approved by HDEQ, August 15, 2005
F1	Closed	17	Clay	Certification Report Approved by HDEQ January 4, 2010
F2	Closed	12	Clay	Certification report approved by HDEQ February 28, 2013
F3	Closed	17	Clay	Certified Closed May 22 2018
D3	Active Disposal	3	Clay	Interim Cover Area
F3/G3	Active Disposal	5	Clay	
G2	Active Disposal	54	Clay	
G1/G3	Unconstructed	56	Clay	
E	Unconstructed	117	Sand	Can be authorized to receive fill once a final closure plan is implemented



**DTE ELECTRIC COMPANY
RANGE ROAD LANDFILL**

2019 SITE PLAN



DRAWN BY:	T Fiebranz
APPROVED BY:	V. BUENING
PROJECT NO.	320507.0000
FILE NO.	320507.0000.01.plt
DATE:	APRIL 2019

FIGURE 1

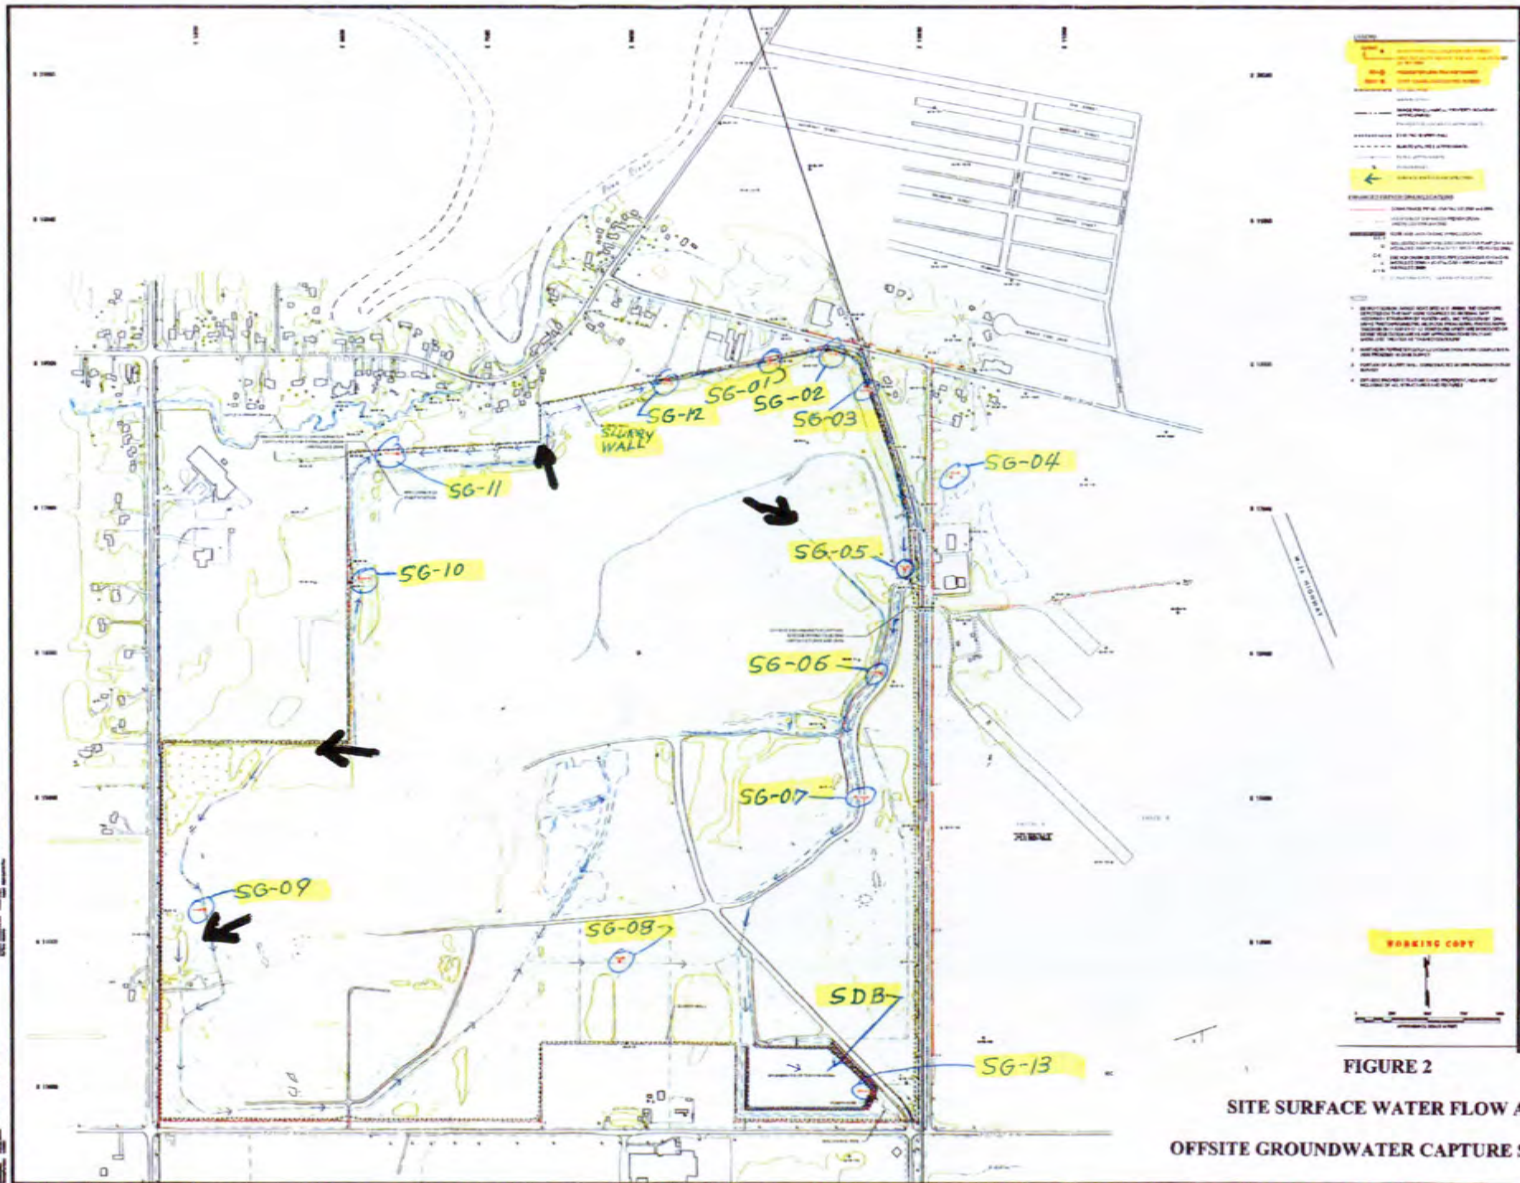


FIGURE 2
SITE SURFACE WATER FLOW AND
OFFSITE GROUNDWATER CAPTURE SYSTEMS

APPENDIX A

Resume of the Qualified Professional Engineer

DANIEL G. BODINE, P.E

**geotechnical and civil engineering
geo-environmental engineering
project management
litigation support
resident engineering
construction management**

EDUCATION

M.S., Geotechnical Engineering, Rutgers University, 1973

B.S., Civil Engineering, Rutgers University, 1970

Continuing Education Seminars

PROFESSIONAL REGISTRATION

Illinois, P.E. Number 0062-047218

Ohio, P.E. Number E-61363

Nebraska, P.E. Number E-9478

Michigan, P.E. Number 6201051139

Colorado, P.E. Number 47434

CAREER SUMMARY

Mr. Bodine has over 50 years of experience in all aspects of civil and environmental engineering. He has worked 13 years for a large AE firm in the civil, geotechnical and site development departments on fossil and nuclear power plant facilities and the remainder time with two major geotechnical and environmental consultants. He has supervised and coordinated fossil and nuclear power plant geotechnical site investigations, foundation and landfill design, construction and post construction activities. He has also performed geotechnical design and construction monitoring work for recent projects for private, industrial, oil and chemical industry, and municipal and government clients. These projects involve design and construction for deep foundations including all types of piles and caissons, several types of barrier walls, site dewatering, insitu solidification and stabilization, runoff collection and treatment basins and landfill liners and caps. He has worked on dam projects such as the Ludington Pump Storage Project, Center Hill Dam Foundation Remediation, AEP's Stingy Run and Amos Fly Ash Dams, CCR Ash Disposal Dikes, Dam Inspections, and numerous other dike and dam safety inspections for the power industry. He has worked with attorneys related to litigation/arbitration and expert witness support related to geotechnical engineering and construction claims. Specialties include barrier wall design and construction, insitu solidification/stabilization, deep foundation design and landfill design & construction including design/build and bid package preparation.

Mr. Bodine's experience on various projects has included the following:

Barrier Wall Technical Report, Confidential National Research Institute. Completed report summarizing approximately 10 types of barrier walls 60-ft deep based on comparisons of their design, constructability, and installation details. Provided construction and QC/QA cost estimates.

Casper Wyoming Barrier Wall, Wyoming DEQ, Casper, WY. Working for the department as a slurry wall specialist providing design and construction document review and comment and attended site review meetings. Barrier wall construction of Phase 1 was completed in 2018 with Phases 2 and 3 to follow. Site was location of former refinery and his review and comments were well received by the lead oil company.

Boeing Design/Build Slurry Wall & Landfill Cap Expansion, Remedial Construction Services, Wichita, KS. Mr. Bodine was Geosyntec's lead technical engineer supervising the preparation of design and construction plans and specifications including technical reports and documents submitted to the KDEH. Served as the technical task manager for the construction QC/QA work including preparation of the construction completion report completed in August 2010. The slurry wall and landfill cap extension, located adjacent to the Arkansas River, surrounded a closed landfill and was constructed without opening the landfill clay cover. Monitoring well water level drawdown on the down-gradient side along the river was noted by owner to drop almost immediately after completion of construction. This has been verified 1 year later, except during periods of river flooding that raises water levels outside of the wall containment.

US Forestry Holden Mine Barrier Wall, U.S. Forestry, Chelan, WA. Working through USF Consultant, Hart Crowser, Mr. Bodine provided specialist consulting review for design and construction of deep 70-100 ft slag & Portland cement bentonite slurry wall located along river and tailings piles at a closed copper mine in middle of a national forest. Work included review of mix design and compatibility testing, construction procedures and quality control test results. Mr. Bodine provided onsite observation and review for US Forestry and their consultant. Field work was completed in 2015.

Ash Reservoir Dam Modification, AEP, Cheshire, OH. As part of the design and permitting work for the closure and capping of a large ash reservoir the 100 ft high dam is being modified by reducing the dam height and providing a new discharge spillway structure for safe discharge of the 100-year and PMF storm flows. Mr. Bodine is the Engineer of Record for the dam modification with construction of a large concrete spillway and full dam and reservoir capping completed at the end of 2020.

Wood River Refinery Sludge Basin Closure, Shell Oil Products, USA, Wood River, IL. As PM and EOR completed an oil refinery engineering design, bid document preparation and construction engineering involving in-situ solidification and capping of over 300,000 cubic yards of oily sludge for an in place RCRA closure of a 20-acre oil

refinery sludge disposal basin located in Wood River, Il. This project is unique in that there is approximately 550,000 cubic yards of sludge in the basin and that the design, permitting and construction was successfully completed saving millions of dollars over alternative closures. Design involved detailed geotechnical settlement analyses of the soils and sludge. Closure construction was completed, and certification report issued to the client and IEPA. Mr. Bodine supervised the CQA monitoring and prepared and sealed the CQA certification report.

Steel Facility Landfill Cap & Tar Pond Solidification, Confidential Owner, NW IN,. Working for contractor provided CQA project management, site work and construction certification of an approximate 60-acre landfill containing two large tar ponds. Geosyntec performed onsite CQA observation, testing, documentation and preparation of the construction completion report including onsite testing of tar solidification /stabilization activities. Project substantially completed in 2014 with Construction Completion Report issued in early 2015. Report for the landfill closure was approved by agency without comment.

BP-Amoco Refinery Sludge Basin Closure, Amoco Corp., Whiting, IN. As EOR and lead engineer supervised design and prepared and evaluated construction bid documents for in-place closure of an oil refinery sludge disposal basin. Design included providing demolition of structural and mechanical equipment, slurry and grout cutoff wall containment, insitu solidification of the sludge, design of wells and pump control systems for surface water collection and as back-up for water level control beneath the solidified sludge. The design included a thicken RCRA type cap with HDPE and soil covers. Also managed CQA and resident engineer construction oversight for the project, including setup and operation of on-site project meetings and laboratory testing operations. The design and oversight included structural work (concrete, steel and asphalt), electrical and mechanical work (wiring, piping, pumps, motors, and controls in accordance with refinery standards) as well as geotechnical and environmental work. Closure of this project under jurisdiction of U.S. EPA Region 5 and IDEM was completed in July 1992 on schedule for Amoco Oil located in Whiting, Indiana. Test program and certification reports for these agencies were prepared under the direct supervision of Mr. Bodine. The thicken RCRA cap was designed, permitted and constructed to accommodate future structures on top of the landfill closure, prior to the widely-used Brownfield concept. Twenty-two years later new structures have been constructed and the new foundation settlement design remains consistent with the original design.

Bofors Nobel Superfund Site, PSDs, Muskegon, MI. Geosyntec PM and EOR responsible for design and management of barrier wall and chemical sludge lagoon cap for the Bofors-Nobel superfund project located near Muskegon, Mi. Work included field and laboratory investigation work plan, 30%, 95% and 100% design, construction

bid package preparation and construction and CQA documentation and performance of barrier wall onsite. Barrier wall construction was Phase 1 of the work and is 100% complete. The wall consists of a soil-bentonite (SB) slurry wall approximately 75 to 125 ft deep and 2000 ft long. Closure cap design and construction of 10 chemical sludge lagoons (portion of Phase 2 work) was completed in 2007. Mr. Bodine was the lead geotechnical engineer for the Phase 2 work, on the Parsons team. Other consulting team members provided team project management, conducted groundwater monitoring and treatment, designed and monitored construction of the treatment and diffuser wetlands, and phytoenhancement of the lagoon cover and surrounding area. Geosyntec assisted these team activities and provided geotechnical portions of the work.

Design & Construction of Permeable Reactive Barrier (PRB) Slurry Wall, Quantum Murray, LLC, Ontario, Canada. Worked as the contractor's slurry wall specialist and prepared contractor plans and technical memorandums for bench scale testing and mix design and construction quality control testing and monitoring procedures for a slurry wall that included design sheet pile control structures for the reactive material. This was for a funnel & gate PRB wall within soils and ground water impacted with radiation. Provided recommendations for onsite construction procedures and QC training of personnel performing slurry and soil-bentonite backfill mixing and testing. Project is completed, performing exceptionally well and is confidential.

Colorado Soil-Bentonite Slurry Wall Construction, Tri-Districts, Ft. Collins, CO. Responsible Project Manager and Lead Engineer for bid document preparation and construction of a 5400 ft long slurry wall around former sand, gravel and cobble pit. Project completed in September 2013 with both contractor construction and engineering oversight completed on schedule and under budget. A 90-day leakage test was performed by an independent consultant and exceeded all requirements by the state.

Gavin Power Plant Residual Waste Landfill Expansion, AEP, Cheshire, OH. Part of the project design team preparing a permit to install (PTI) package for the lateral and vertical expansion of a 58,000 cubic yards waste landfill. Performed design reviews of plans, drawings and specifications, including leachate treatment ponds and assisted in major field investigation program that had to be performed thru-out the winter months and during the holiday period. The PTI was approved and formal permit issued in early 2014. Construction packages for the landfill expansion were prepared and construction of Phases 1 and 2 have been completed. Additional construction phases are underway.

Detroit Edison Power Company Ash Basin Evaluation & Design Modifications, Monroe, MI. Performed dike inspection of large ash basin to assist in evaluation of a large number of shallow slope failures. Project work included prepared construction plans and specifications for repair and reconstruction of slopes and related drainage facilities. Provided quality construction expertise for the 2009, 2010 and 2011

construction phases, all now completed. Mr. Bodine consults on designs as needed with team members on other site projects for DTE.

Detroit Edison Power Company Ash Basin Drainage Ditch Evaluation & Design. Managed and performed design of a large drainage ditch which is part of the Range Road Landfill existing ash basin that involved culvert alternatives including a large diameter structural pipe arch. Project completed in 2010.

DTE Energy Range Road Landfill Annual Inspections, St. Clair, MI. Conducted field inspection and office file review under the CCR Rule 40 CFR 257.84(b)(1) for the Range Road 418-acre landfill. The annual inspections and reports were for years 2015, 2016, 2017, 2018, 2019, 2020, 2021 and 2022.

American Electric Power Dam Inspections. Providing multi-year (1999-2001) independent annual dam safety inspections and reporting of dike and dam structures at 18 facilities for American Electric Power in the states of Indiana, Ohio, Kentucky, West Virginia and Virginia. Dams range from small dike containment structures to large high hazard classification dams. Internal inspections and repair recommendations for discharge pipes were also provided at 3 AEP facilities. Reports for the utility and state agencies were prepared for all facilities. Prior to this project Mr. Bodine performed dike and dam inspections of ash disposal and power plant lake facilities in the states of Illinois, Wisconsin, Indiana, Ohio, Kentucky, Colorado and Texas.

CCR Location Restriction and Groundwater Monitoring Network Reports. AEP, Ohio. Provided CCR facility evaluation and report preparation for Location Restriction Evaluation at two separate AEP plants. Assisted the Groundwater Monitoring Network report preparation and review for the same two plants.

CCR Alternative Source Demonstration (ASD) and Assessment Reports. Buckeye Power, Inc., Ohio. Part of Geosyntec's team in preparing ASD reports for an RSW landfill and assessment and monitoring report for a bottom ash disposal basin at Buckeye's Cardinal Plant. Geosyntec's ASDs monitoring work is ongoing at this plant site and other sites for other power clients.

Indianapolis Power & Light Ash Pond Dike Inspections, Indiana. Provided ash pond facility inspection in 2008 for three coal fired power plant sites. Prepared inspection report findings and recommendations for maintenance and for critical dike re-evaluations.

Sylvan Lake Dam Evaluation, RCCD, Rome City, In. Performed dam and spillway inspections and report for 2004 through 2022 at Rome City, Indiana. In 2004 Geosyntec prepared a special dam evaluation report reviewing a critical Dam safety report prepared by U.S. Army Corps of Engineers. In 2007 consulted with dam owner during periods of very heavy rainfall concerning opening of emergency flood gate, however, it was not necessary to open the gate. Attended and took part in the

Emergency Action Plan table-top-exercise in 2007, 2011, 2016, 2018 and 2021. Prepared the project O&M Manual and provided owner training and annual inspection activates since 2004. Remain as Rome City's on-call engineer with respect to dam safety and inspection.

Ash Reservoir Dam Modification, AEP, Cheshire, OH. As part of the design and permitting work for the closure and capping of a large ash reservoir the 100 ft high dam is being modified by reducing the dam height and providing a new discharge spillway structure for safe discharge of the 100-year and PMF storm flows. Mr. Bodine is the Engineer of Record for the dam modification with construction substantially completed in 2020.

Cardinal FAR 1, AEP, Brilliant, OH. As EOR responsible for Geosyntec design and major permit document preparation for a 127 acre 18 million cubic yards FGD gypsum landfill at a power plant facility in the State of Ohio. Major portion of new landfill is to be constructed over an existing closed fly ash disposal area. Design and permit documents included detailed geotechnical settlement and stability analyses. Agency has completed review and permit was issued in April 2007. Construction of Cell 1 was completed and a minor permit modification to construct Cell 3 before Cell 2 was prepared with agency approval in 2008. Preparation of Cell 3 construction drawings was completed in 2010 and cell construction followed in 2011. Waste filling is ongoing.

Chicago Public Building Commission (PBC), Chicago IL. Provided review of construction documents and prepared report on lessons learned for a new school project that involved construction dewatering, excavation and earth retention that resulted in schedule delay and some foundation redesign. Consulted on means and methods for turning around dewatering and excavation problems. With other Geosyntec team members worked on several other PBC projects related to dewatering, earth retention design and permitting, including one high profile downtown Chicago project. Other PBC projects (library & athletic field house) included preparing and reviewing foundation designs for the architect/engineer and performing foundation inspections.

CSX Talleyrand, CSX, Jacksonville, FL. Served as senior reviewer and in-house barrier wall consultant for design and construction of a Florida landfill slurry wall approximate 43 feet in depth. Designed and summarized the slurry wall compatibility and mix design testing program and trained others on the design and onsite for the slurry wall quality control/quality assurance testing and inspection. Site is unique because of high groundwater adjacent to a river, adjacent to a major city sewer line, and included a large portion of excavation within peat soils. Wall was completed in summer of 2011 and landfill cap late in 2011.

CSX Richmond, CSX, Richmond, VA. Serving as senior reviewer and in-house consultant on slurry design and permitting for 40 ft deep soil-bentonite wall at a former

wood treating facility in Richmond, Virginia. Project design and review by the US EPA and VA DEQ is final. The slurry wall construction was started and completed in 2014.

Former Camilla Wood Preserving Site, Black & Veatch, Camilla, GA. Providing barrier wall consulting and in-house recommendations for design team on slurry wall compatibility testing and response to US EPA questions. Conventional soil-bentonite wall was selected and wall construction completed in 2013.

O'Hare Airport Stormwater Flood Control Reservoir, AOR, City of Chicago, IL. Provided technical review of existing reservoir design by others during construction to assist in solving design/construction problem involving slope seepage and erosion. Geosyntec provided recommendations for design changes and repairs, as well as additional monitoring to prevent slope erosion and reduce uplift pressures to acceptable factors of safety.

O'Hare Airport Stormwater Damage Mitigation Measures, CARE, Chicago Department of Aviation, Chicago, IL. Technical lead providing investigation, evaluation and corrective measure design of stormwater related seepage damage to an underground training area located adjacent to an existing airport utility tunnel. Designed concrete retaining wall repairs and preventative measures to collect and transfer excessive groundwater during and immediately after stormwater events from causing future similar problems.

Rt 44 Barrier Wall, Tauton, MA. Served as in-house consultant for an 800-foot long, 50-foot deep slurry wall installed to contain contaminants present in the saturated portion of the soil. Barrier wall was part of an overall drum removal and thermal desorption project. Provided onsite monitoring and training of others for the slurry wall quality control/quality assurance testing and inspection. Wall was completed in 2010.

McColl Superfund Site, CA. Served as in-house consultant and mentor for the field monitoring and site engineering of the slurry wall construction phase. Provided daily contact as needed for the two soil-bentonite slurry walls that transverse sloping topography and were tied into the final cover system.

Home Depot Site Redevelopment, Burbank, CA. Geosyntec provided concept and detail design, construction, operation, maintenance and monitoring of site remediation of a dual-phase extraction (DPE) and soil vapor extraction (SVE) systems at a redevelopment site. Part of the design included a 2,600 ft long, 55 ft deep soil-bentonite slurry wall. Mr. Bodine consulted on the design and led the construction quality assurance monitoring and testing of the barrier wall.

138th Street Landfill. Land And Lakes, Dalton, IL. Performed full time Resident Engineering and Construction Management for landfill client on an IEPA remedial action project located on the southeast side of Chicago. Project involved earthwork, slurry wall and leachate collection and transfer systems installation. Duties included

review of project submittals, contractor invoices, CQA activities, preparation of progress reports, design modifications approved by the designer and preparation of the Construction Completion Report. Construction project was brought-in under budget.

Historical Slurry Wall Design & CQA. Provided full-time construction quality assurance activities for landfills and cooling lakes with slurry and grout (cement and chemical) cutoff walls, including preparing summary CQA reports. Cutoffs have performed exceptionally well, some for over 40 years. Slurry wall experience includes shallow and deep Soil Bentonite and Cement Bentonite walls, specification preparation, and full time CQA/CQC activities for approximately 1.5 million square feet of wall. Recent projects involved environmental remediation and closure at landfill and disposal projects where construction dewatering, containment and site closure were involved. Another involved slurry wall design and specifications for groundwater and flood control for a 4-lane state highway project with railroad and river overpass crossings. Total slurry wall experience involves walls totaling over 25 miles long. Completed local Midwest projects with deep walls (>50 ft and <130 ft) include Schaefer Power Station in Indiana and Braidwood Nuclear Power Station in Illinois and the Bofors Nobel project mentioned above. Projects with medium depth cutoff walls (>30 ft and <50 ft) include Collins Power Station in Illinois and Amoco Oil (now BP) Refinery in Indiana. The Amoco walls (4 total) involved cement bentonite, jet grout and chemical grout barriers. Specification and CQA monitoring review for soil bentonite walls was also performed for the McColl Superfund project and a Home Depot project in California. Two of the recent slurry walls have been design/build projects where Mr. Bodine, in addition to design and project management activities, supervised the QC/QA work and certified the construction. The Amoco project is discussed in a paper listed at the end of this resume. Copy provided upon request.

Groundwater Remediation System CM and CQA, Shell, Kankakee, IL. Provided design and construction bid document and specification review for a bedrock groundwater interceptor trench and surface water collection basin and controls. Performed CM and CQA activities at the site and prepared a project construction certification report. Reviewed all contractor draft invoices and assisted client negotiating settlement of work claims and revised contract when project changed from non-union to union labor and operator work. Project was successfully completed and performing as intended.

Naval Training Center and Power Plant Site, TN & Associates, Newport, RI. Mr. Bodine has prepared designs, plans, specifications, and monitored installation and testing for numerous pile and drilled shaft construction projects. Most current pile installation and load test monitoring occurred in 2006 at the Newport Naval Training Facility in Newport Rhode Island. Selected, monitored and evaluated dynamic pile testing and a static load test at site of Fuel Oil Tank No. 2. Pile testing was successful and exceeded design requirements.

DOE Fernald Onsite Disposal Facility, Flour, Fernald, OH. Performed duties as responsible onsite Resident Engineer for construction of the leachate conveyance system and two onsite disposal facility (OSDF) cells at DOE's Fernald Environmental Management Project, located near Cincinnati, Ohio. Systems included structural, geotechnical, mechanical, electrical and environmental equipment. Duties included review of contractor submittals, preparation, review and approval of design modifications, preparation of reports, interaction with client and contractor construction management, engineering and quality assurance personnel and project's CQC staff. Cell 1 began accepting impacted material in 1997. During 1998 Mr. Bodine performed the duties of Geosyntec's onsite Managing Engineer and Certifying Engineer during which time filling of Cell 1 with low level impacted materials and construction of Cell 2 was completed. All 8 Cells of the OSDF were completed by end of 2006 ahead of schedule.

Willow Ranch Landfill Retaining Wall, Land And Lakes, Romeoville, IL. Provided Construction Management assistance and Construction Quality Assurance monitoring and Engineering Certification of the installation of a geogrid tieback concrete retaining wall located at a closed landfill site. The wall consists of 700 lineal feet of panels with 3 and 4 stepped levels, constructed at a 7 percent alignment grade. One hundred and seven (107) concrete panels twenty-foot long were formed, constructed and installed on site. Construction submittals, schedules and testing for concrete and soils was provided.

Elgin Illinois Landfill Closure, BFI, Elgin, IL. Managed CQA monitoring and provided CQA certification of Closure of Elgin Landfill Superfund Site located in Kane County, Illinois. Closure design by US Army Corps of Engineers (US ACE) involved a soil and geosynthetic cap. Project fieldwork completed end of Nov. 2001 and the remedial construction completion report (RCCR) prepared in Dec. 2001. The US EPA and Corps without comment approved the RCCR. For the same landfill closure Mr. Bodine prepared the Operation and Maintenance Plan that involved normal landfill maintenance, long term groundwater monitoring and operation of the landfill gas management system.

City of Janesville Wisconsin Landfill, Provided management of project consisting of the review and evaluation of a poorly performing landfill gas system, and the design of a new dual well gas/leachate collection system. Services included field measurements, preparation of landfill permit modification and construction bid documents with contract requirements, specifications and drawings. Project began in May 2002 with construction of the new dual well collection system completed in December 2002.

Permits. Responsible for preparation and certification of NPDES permits, Construction permits, Joint permits, Dam safety permits, stormwater permits and plans, local permits and other agency documents for flood control projects, wastewater treatment facilities, landfills and various site remediation projects. Selected completed projects include the

Meacham Grove Dam and Reservoir Flood Control Project in DuPage County Illinois and permitting activities for BASF, Amoco Chemical and Exxon Chemical.

Boston Tunnel Construction Claim, CAT, Boston MA. Provided expert witness support for major geotechnical construction claim. Work consisted of technical assessment of contractor claims for extra compensation for excavation of Central Artery Tunnel. Mr. Bodine was a key member of the assessment team that resulted in full rejection of the \$25 million claim against the CA/T project.

Scottsville Landfill Construction Claim, Scottsville, MI. Provided technical assessment of construction claim for new landfill construction in the State of Michigan. Assessment resulted in nearly full rejection of contractor claim for 2 to 4 million of extra compensation for earthwork construction and schedule extension.

Unloading Dock Construction Claim, Honduras. Performed independent review of geotechnical foundation investigation and design for pile foundation for arbitration hearings concerning significant design-build cost extras for a large docking facility located in Central America.

Power Plant Circulating Water Pipe Evaluations, NW IN. Provided confidential evaluation of two large 14-ft diameter CMP pipe collapses for an AE designer and assisted field sampling and evaluation of two other power plant CMPs for long term integrity condition evaluations.

Foundation Site Investigation and Geotechnical Design. During the 1970's and 1980's coordinated site investigation and geotechnical foundation design of power plant and waste disposal structures for several fossil units between 500 MW to 750 MW in size located in the Midwest and South. Foundation and pond design included shallow and deep foundations (piles, caissons and drilled shafts) and water and waste holding ponds and dikes. The deep foundations were subject to a large range of loading conditions and conducting several large-scale load tests where necessary. One major project located along the Mississippi River in Louisiana is discussed in a paper listed at the end of this resume. Projects specific to Illinois and Indiana included those at several plants designed by Sargent & Lundy during the period.

Safety Analysis Report Preparation. Supervised and prepared geotechnical foundation design criteria and geotechnical and groundwater sections of safety analysis reports (SARs) for nuclear power plants located in Illinois, Indiana, and South Korea.

Cooling Lake and Dam Inspections. Conducted cooling lake and dam inspection and monitoring activities for lakes up to 3000 acres in size and over 25 miles of embankment dikes or dams. Prepared reports for submittal to client and appropriate state and federal agencies. The largest of these projects (Braidwood Nuclear Power Station Cooling Lake) involved dike construction and cutoffs constructed over and through extensive coal strip-mine spoils and over underground coal mines. Site

monitoring included settlement monitoring of pre-load and dike fills over strip-mine spoils up to 120 ft thick, slope indicator movements, piezometer measurements and sampling for seepage and water quality evaluations.

SWMU's at Argonne National Lab, Illinois. Performed Visual Site Inspections and Structural Integrity Assessments for a large number of Solid Waste Management Units (SWMUs) at DOE's Argonne National Laboratory-East as part of a corrective action program under RCRA. Performed duties as the Certifying Professional Engineer.

PROFESSIONAL EXPERIENCE

Geosyntec Consultants, Chicago/Oak Brook, IL, June 1996-Present

Woodward-Clyde Consultants, Chicago, IL, March 1989-June 1996

Sargent & Lundy Engineers, Chicago, IL, 1976-1989

Woodward-Clyde Consultants, Clifton, NJ, 1970-1972, Chicago IL, 1973-1976

PROFESSIONAL AFFILIATIONS

American Society of Civil Engineers - Life Member - Geo-Institute

Illinois Society of Professional Engineers (ISPE)

Deep Foundation Institute (DFI)

Three Rivers Manufacturing Association (Industry Association)

REPRESENTATIVE PUBLICATIONS

“Implementation of a Permeable Reactive Barrier for Treatment of Groundwater Impacted by Strontium-90”, Andrzej Przepiora, Dan Bodine, Peter Dollar and Jim Coughlin, *The 19th Pacific Basin Nuclear Conference (PBNC 2014)*, August 24-28, 2014, Vancouver, Canada.

“Analysis and Verification of Louisiana Pile Foundation Design Based on Pressuremeter Results”, D.G. Bodine and R. R. Davidson, in *The Pressuremeter and Its Marine Applications*: American Society for Testing and Materials, 1986.

“Effects of Clay Swelling on Permeability Calculations Obtained From Sealed Double Ring Infiltrometer Tests”, C. B. Avci, D. G. Bodine and E. Guler, in *The First International Congress on Environmental Geotechnics*, Edmonton, Canada; July 10-15, 1994.

“RCRA Closure of Refinery Sludge Basin Using In-situ Solidification and Containment”, D. G. Bodine and F. M. Trevino, in *The Proceedings of The Fourth Great Lakes Geotechnical/Geoenvironmental Conference: In-Situ Remediation of Contaminated Sites*, Krishna R. Reddy, Editor, University of Illinois at Chicago; May 17, 1996. Containment was by cement bentonite slurry wall and cement bentonite jet

grout wall on the shore of Lake Michigan.

“Design and Permitting of a FGD Landfill Over and Existing Ash Reservoir” (2009), D. G. Bodine, B. F. Tanyu, P. J. Sabatini, M. A. Ajlouni and D. E. Limes, Geotechnical Special Publication No. 187, Contemporary Topics in Ground Modification, Problem Soils, and Geo-Support, pp. 496-503.

“Case Study: Stability of Two Horizontal to One Vertical Embankment” (2011), Tanyu, B. F., Neal, W., Seymour, J. P., Bodine, D. G, Bozok, O., Paper presented at the ASCE Geo-Frontiers March, 2011, Dallas, Texas.

APPENDIX B

Range Road Landfill Annual Inspection Log

Range Road Landfill Annual Inspection Photographs

Detroit Edison Company Range Road Ash Disposal Facility Annual Inspection Log

Inspector: Dan Bodine, P.E., Geosyntec
DTE: Jason Roggenbuck Provided Documents
and Accompanied Field Inspection
 Date: 19 April 2022, 7:00-1 pm

Weather: Cloudy
Temperature 31°-44 F, Light Wind

Previous P.E. Annual Inspection Date: 19 April 2021

Item	Condition			Related Photo # (s)	Notes and Comments (LDP=Landfill Development Plan)
	Good	Adequate	CA Req.		
General Site					
1. Site Access Restricted / Attendant On-duty	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Visitor Sign in	Gates locked, except active ash haul road entrance near Guard. Additional security and health checks at Plant Gate Check-In.
2. Security Fence / Gates	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Gates 10, 14, 28 & 49	Good. Main Gate not shown, but Manned Guard Shack Across Street. Landfill Gate lockable. All Other Gates had Signs & Locked.
3. Signs and Markers	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	10, 8, 14,19, 28 & 49	Signs/markers were present at most gates and entrance. Road edge markers shown in Photos 41 & 42. AST signs shown Photo 35
4. Access Roads and Construction Site Roads	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	10, 13, 18, 20, 25, 28, 47, 50 & 53	All very good. No road access problems even with very light snow night before.
5. Traffic Flow and Waste Unloading	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	44	Haul trucks operating and unloading Safely
6. AST Inspection	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	8	Appeared Good. One of the two tanks has been removed.
7. Universal Waste (properly labelled, container condition, less than one (1) year from accumulation start date)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	None provided	Sources noted in previous documents reviewed.
Waste and Nuisance Control					
8. Ash Hauling Contractor On-site Safety/Training	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	None provided	Contractor Site Office closed. DTE indicated no new personnel.
9. Ash Hauling Contractor Equipment Condition/Adequacy	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	44, 45	Equipment appeared acceptable but were not inspected closely as part of our requirements. No inspection documents provided.
10. Ash Hauling Contractor Filling Active Area to Appropriate Grade	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	31, 32, & 37	Visual observations indicated Contractor filling activity acceptable and G2 Phase I capping acceptable except final seeding and gully repair occurred after inspection. Closure certification report was transmitted after inspection along with EGLE approval letter.

Detroit Edison Company
Range Road Ash Disposal Facility
Annual Inspection Log

11. Waste Condition (i.e. - waste from approved source, no recyclables, no MSW, no liquids, no hazardous wastes, etc.)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	44 & 45	Waste being delivered appeared acceptable and from approved source as indicated by DTE Inspector.
12. Noise Level	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		Covered in LDP. No Contractor noise noted at perimeter areas within Landfill during Inspection. 2021 November Annual Report
13. Dust Control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		Dust Control Plan and Annual Report available. One complaint and action taken. November 2022 Annual Report Reviewed.
14. Adequacy of Interim Cover and Interim Stockpile Cover	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		No Interim landfill cover area observed this inspection. Area G2 Phase I construction certification report transmitted after annual inspection along with ELGE Area G2 Phase I Certification Approval Letter.
Final Cover					
15. Landfill Side Slope Condition (i.e.-no seeps, no cracking, no settling, no burrows, adequate vegetation)	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	16, 22,27, 29, 30, 36, 39, 40, 41, 42, 43, 46, 47, 53 & 54	Trees on N, NE, NW sides approved to stay and did not appear to cause any observable stability problems. Capped slope of active G2 Phase 1 area shown in Photos 30, 32 & 39 appeared stable (adequate) awaiting erosion repair and/or reseeding and vegetation growth. Erosion repair and reseeding, and vegetation growth now completed as shown in DTE Photos 41 and 42 and slope condition judge Good.
16. Final Cover Top Condition	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	31, 32, 33, 34, 35, 37 & 38	Top and slope final cover areas appeared well vegetated, after spring erosion repair, reseeding and vegetation growth for Area G2 Phase 1 recently capped and seeded. No observed settlement or stability conditions in closed or capped areas. Relatively flat cover designs require swales to direct potential flows to downchutes.
Leachate and Surface Water Control					
17. Stormwater Detention Pond Water Quality (unnatural films, foams, oils, etc.) and pump operating condition (panel, meter etc.)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	3	Quality appeared good. Pumps not running at time of inspection but panel lights not on and no pumps tagged for out of service.
18. Stormwater Detention Pond Side Slope Condition (erosion, riprap, vegetation) and any other operating observations not in 17 above.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	1, 2 & 4	Appeared stable and adequately vegetated & protected. WL also monitored with staff gauge, SG-13.

Detroit Edison Company
Range Road Ash Disposal Facility
Annual Inspection Log

19. NW Corner Lift Station Surface Water Ditch Level & Pump	<input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>	23 & 24	New pumps & sump level controls were installed in late 2017. Some maintenance repair performed in 2021. Pumps and hands-on switches were checked (DTE person) and all appeared operating correctly.
20. NW Corner Lift Station Operating Condition	<input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>	24	See also Item 19 above.
21. NE Off-site French Drain Operating Condition	<input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>	No Photo	Control building locked and DTE Inspector did not have key.
22. NW Off-site French Drain Operating Condition	<input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>		Offsite, not Inspected; Covered in TRC reports. Items 19 & 20 discusses lift station and pump conditions.
23. NE/NW Off-site French Drain Outfall Water Quality	<input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>		Not part of this CCR inspection. Covered in other reports.
24. Perimeter Slurry Wall Marker Condition	<input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>	10 & 28	Slurry wall below Grade and Surrounds Entire Landfill at/near Property Line. Barrier to any below grade GW Flow. Markers show Alignment. Many markers remain however some may have been removed for road upgrades. Slurry Wall as-built location are reported in several reports and on file in DTE office.
25. Perimeter Ditch System (Flow & Staff Gauge Monitoring)	<input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/>	See Item 26 below for the many ditch photos taken.	Almost no flow observed because of low water level conditions. Visual observations of ditch flow conditions appeared satisfactory. Fourth Quarter 2021 and First Quarter 2022 reviewed, and flow directions were good.

Detroit Edison Company Range Road Ash Disposal Facility Annual Inspection Log

<p>26. Perimeter Ditch System (Slope & Bottom Conditions); Includes Internal Ditch if a Main Discharge to Perimeter Ditch</p>	<p><input checked="" type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/></p>	<p>5, 6, 9, 11, 12, 15, 17, 18, 20, 21, 22, 25, 26, 27, 29, 47 & 48</p>	<p>Perimeter ditch located around entire active and closed landfill areas. Major internal ditches also drain to perimeter ditch. Runoff from landfill and runoff from the site is controlled by the ditch system and perimeter slurry wall. Flow appears to be maintained based on review of ditch water elevations. DTE Indicates that non-woody vegetation has been approved to remain as long as flow maintained. DTE maintenance is being provided as needed. Internal ponds also shown in these photos attached.</p>
---	--	---	---

Doc. Title: Range Road Ash Annual Inspection Log. Form Edited with Additions by Inspection Engineer,
Verify Original Version on Belle River Website Prior to use - UNCONTROLLED

Form Original Date:
01/08/15

APPENDIX B

DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



1. Storm Water Detention Basin (SWDB), S & W Sides. Slopes are Protected with Stone. No Visible Slope Erosion on All Sides. Same for N & E Sides.



2. Intake Screens at SWDB with Some Minor Vegetation at Bottom. Water from Basin is Pumped Back to Power Plant Using One or More of 3 Pump3.



3. Pump Control Panel. All 3 Pumps were Available for Use. Wall Flow Meter (Not Shown) appeared OK. Pumps were Observed but not Pumping at the Time.



4. Looking at NE Corner of SWDB. Slope Protected from Erosion with Stone. Staff Gauge SG-13 in Middle of Photo at or Just Above the Water.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



5. Staff Gauge Along East Side. Ditch Open. Light Snow Night Before Inspection.



6. Another Staff Gauge Along East Side. Ditch Flow Open. Observed Past Slope Vegetation Maintenance.



7. Monitoring Well 16-05. Well Protected and Cap Locked. Well Protection and Capping Typical of Inspected Above Ground Monitoring Wells.



8. Single AST at Contractor Onsite Yard/Office. No Leakage Observed.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



9. Flow from Culvert into Perimeter Ditch. Culvert and Ditch Remain Open.



10. View of Locked Gate with Signage. All Gates observed had Signage and were Locked.



11. Looking at Staff Gauge Location Along Northeast Corner. Ditch Open but Flow not Observed. Some slope drainage into ditch.



12. Perimeter Ditch at Corner with Vegetation but Still Open.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



13. Monitoring Well and Perimeter Road Along Northeast Corner. Road in Good Condition and Well Locked.



14. Another Perimeter Fence Gate Locked and Signage Postage. Gates Only Used for Maintenance Access if Necessary. Piezometer 96-W-12R, Locked.



15. Locked Piezometer PZ-01R and Staff Gauge Location.



16. Wooded Area Between Ditch and Landfill Area B.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



17. Looking at Location of Staff Gauge SG-01. Water Present. No Visible Flow Noted.



18. Ditch Alignment and Perimeter Road in Good Condition. Trees Along Outside Slope of Closed Landfill Areas at North End of Landfill.



19. Locked Piezometer W-01R Along Perimeter Road and Perimeter Fence, Note Fence Signage.



20. Culvert and Riprap Downslope Where Ditch Clearing of Vegetation Had Been Performed in 2021. Flow did not Appear to be Blocked.

APPENDIX B

DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



21. Bottom of Downchute Shown in Photo 22 Drains Through Culvert to Perimeter Ditch Along Perimeter Road.



22. Looking Up Along Landfill Surface Runoff Ditch Downchute Protected from Erosion with Riprap. Flow Drains into Ditch Culvert in Photo 21.



23. Sump Pumps in Manhole. New Pumps were Installed In 2018. Discharge to Culvert Connected to Ditch. Inlet Pipe Shown Little Flow.



24. Neither Pump Running and in Hand Operation Per Panel Controls. DTE Inspector Manually Verified Pumps Operation. Controls Restored to Auto.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



25. Ditch Open and Not Blocked but Some Vegetation Shown in Center Area of Ditch Photo. Culvert Open.



26. Note Circular Light Brown Sand in Ditch Indicating Possible Discharge Location of a Downslope Location of Small Below Grade Discharge Pipe.



27. View of Perimeter Ditch Past Maintenance with Small Riprap Check Dam. Ditch Slope Maintenance has been Completed Previously.



28. West Side Access Fence, Locked and Signage Posted. Perimeter Slurry Wall Marker Shown.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



29. Downchute Located at Southwest Corner of Landfill Area F1. Chute Protected from Erosion with Riprap & Steel Mesh. Some Slope Bottom Erosion Noted.



30. Western Side of Area G2 Graded and Seeded. Some Minor Slope Runoff Erosion Shown and Should be Observed and Inspected As Vegetation Grows.



31. View of Top of Landfill Area G2 Phase 1 that has been Graded and Capped in Accordance with Landfill Cover Design. Initial Seeding Completed.



32. Top of Landfill Area G2 Phase 1 Along West Side Slope where Grading and Initial Seeding had Taken Place in Fall of 2021.

APPENDIX B

DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



33. Top of Closed Landfill Areas Well Vegetated and Mowed in 2021.



34. Top of Closed Landfill Areas Well Vegetated and Mowed in 2021. Isolated Past Small Brush/Tree Growth has been Removed.



35. Another View of Top of Closed Landfill Areas where Top was Mowed in 2021. Mowing of Complete Final Cover was a Major Maintenance Activity.



36. Central Runoff Holding Ponds. No Blockage Observed and Ditch Vegetation Appeared Satisfactory Although Not Walked Due to Slip, Trip & Fall Safety.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



37. View of Top of Capped Area G2 Phase 1. Cover Initial Seeding was Completed but Necessary Re-seeding in Spring 2022 was Completed.



38. Surface Drainage Swale Top Area G2 Phase 1 with Slope into Phase 2. Some Rutting but Repair/Re-seeding Completed in Spring 2022, per DTE.



39. East Side Slope of Capped Area G2 Phase 1. Slope Erosion Gully. Cover & Slope Repair & Re-Seeding Completed in Spring. See Photos 40, 41 and 42.



40. DTE Photo of Area G2 Phase 1 Slope Erosion Gullies Repaired and Re-Seeded in Spring 2022 after April Annual Inspection.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



41. DTE Photo of Area G2 Phase 1 Slope after Seeding Growth and Typical of Slope and Cover Seeding and Spring Re-Seeding.



42. DTE Photo of Area G2 Phase 1 Downslope Drain from Cover Swale on Top of Cover.



43. Runoff Pond Constructed Southeast of Active Area G2 Phase 2.



44. CCR Haul Trucks Safely Unloading What from a Distance Appears to be Bottom Ash and/or Fly Ash. Active Area G2 Phase 2 Shown.

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



5. Active Area G2 Phase 2 Construction Equipment Working. The Light Snow Cover Occurred the Day/Evening Before.



46. Light Snow Cover East Side Slopes of Areas Fe and G2 Phase 1. Slopes Appeared in Good Condition & Stable. See Erosion Gullies Shown in Photo 42.



47. Haul Road in Excellent Condition and Internal Drainage Ditch Outside of Landfill Silt Fence. Silt Fence in General Satisfactory Condition.



48. Construction Fencing Around Landfill G2 Areas. Internal Drainage Ditch Located Forefront of Photo (Same Ditch as in Photo 47).

APPENDIX B
DTE Electric Company Range Road Landfill Annual Inspection 19 April 2022



49. Photo Taken from Highway of Locked Gate Only Used for Special Construction or Maintenance Entrance. Monitoring Well No. 16-05 Inside Fence.



50. Haul Road to Top of closed Portions of Landfill Between D and F areas.



53. DTE Photo of Haul Road to Top of Final Cover with Runoff Collection Ditches Either Side of Road. Previous Re-Occurring Slope Erosion Right Side.



54. DTE Photo of Repair with Added Riprap and Slope Erosion Repair/Re-Seeding. Note Silt Fence at Top where Surface Runoff Meets Slope.
